

# Building for the Future

June 2025 Update



**Dear Friends,**

Thank you for your continued prayers and support for our building project.


## Renovation Works

Since our last update in April the renovation works have progressed well.

Downstairs, all the internal partition walls have been erected, plastered and painted. First fix electrical is complete, and second fix is continuing. The plumbing has been started, and the toilets and kitchen have been tiled. Some unforeseen works were needed downstairs to provide enhanced fire protection around structural steelwork that supports the upstairs floor.

Upstairs, the partition wall modifications are 75% complete, and the first fix electrical work is ongoing. Unforeseen works were needed to extend some partition walls from ceiling height to roof height. Additional ventilation works are also required. We also had to make some layout changes to comply with the requirements of the planning regulations. We therefore needed to apply for a Revised Fire Certificate from Mayo County Council. A decision on this application is due at the end of July, but we hope to receive it earlier.

We are grateful for our professional builders and tradesmen who are working well together. We are also grateful to teams of volunteers from Men4Mission and UFM, and for many of our own members who have volunteered their time.

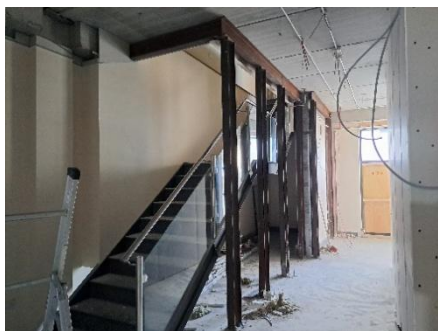

## Financial Update

To date we have raised €433,395.

Current estimates are that we will need approximately an additional €20,000 to €25,000 to complete the legally required works, and a further €40,000 for finishes and furnishing.

We are having a special offering in our church on Sunday 6<sup>th</sup> July.

If you or your church would like more information please get in touch. To donate towards this project, please click the following link: [www.calvarychurchclaremorris.ie/donate](http://www.calvarychurchclaremorris.ie/donate)

## Renovation works

Our schedule is roughly as follows:

### Phase 1: Legally required works

- Fire and disabled regulation works
- Ventilation
- Main plumbing and electrical works

Complete July 2025

### Phase 2: Finishes and furniture

- Complete internal fit out
- Woodwork
- Floor and wall finishes and decorating

Complete September 2025

## Volunteers

To help progress the project and keep costs down, we would appreciate help from volunteers for the following tasks:

- Insulating and plaster boarding
- Installing ventilation
- Carpentry including fitting doors and skirting board
- Plastering

If you are able to help in these areas, please do get in touch.

*Thank you for your continued prayers and support for this project.*
